



Trail Day 17 November 07



Priority 1 Downhill Reroute


Complete cutting in trail

Fix areas crossing ruts

- Bridges in ground
- Fill in areas and reinforce

Close old downhill

- Silt screen
- Large relief cuts
- Throw down grass seed

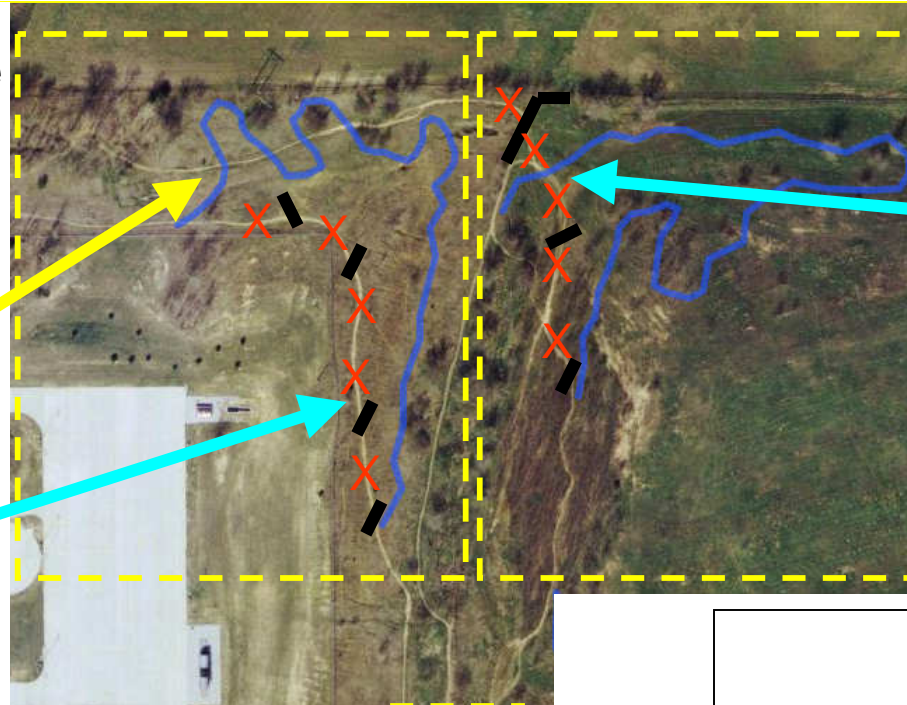

Priority 3 Trail Extension

Complete cutting in trail

Fix areas crossing ruts

Close old trail section

- Silt screen
- Throw down grass seed

Silt screen corner

Priority 2 Restore drainage to culvert

Dig a ditch for water to drain into culvert and rebuild old water control berm.

Fill in erosion created ditches

Close the old turn in the culvert



Legend

New Trail 

Closing trail 

Silt Screen 

Erosion Control 
